



Vaden Drive Bridge - Final Construction Update


Construction of the new Vaden Drive Bridge over I-66 is nearing completion. The final concrete pour for the new bridge deck is scheduled to occur on Friday, October 9. Once the concrete bridge deck has cured, crews will lay the final asphalt approaching the new bridge deck, finish work on the sidewalks and parapets, and install the bridge railing and fencing.

Work to rebuild and repave Vaden Drive north and south of the bridge over I-66 will begin the week of October 12. This work will involve earthwork, backfilling for the bridge abutments, installation of drainage, utility relocation, and curb and gutter construction.

Beginning in early November (exact date to be scheduled and weather dependent), the Vienna-Fairfax/GMU Metrorail Station north and south parking garage entrances located on Vaden Drive will be closed for approximately two weeks for the final paving work. Access to North Garage will remain from Virginia Center Boulevard and access to South Garage will remain from Saintsbury Drive.

The new bridge is planned to open to traffic by mid-November 2020.

Construction Timeline

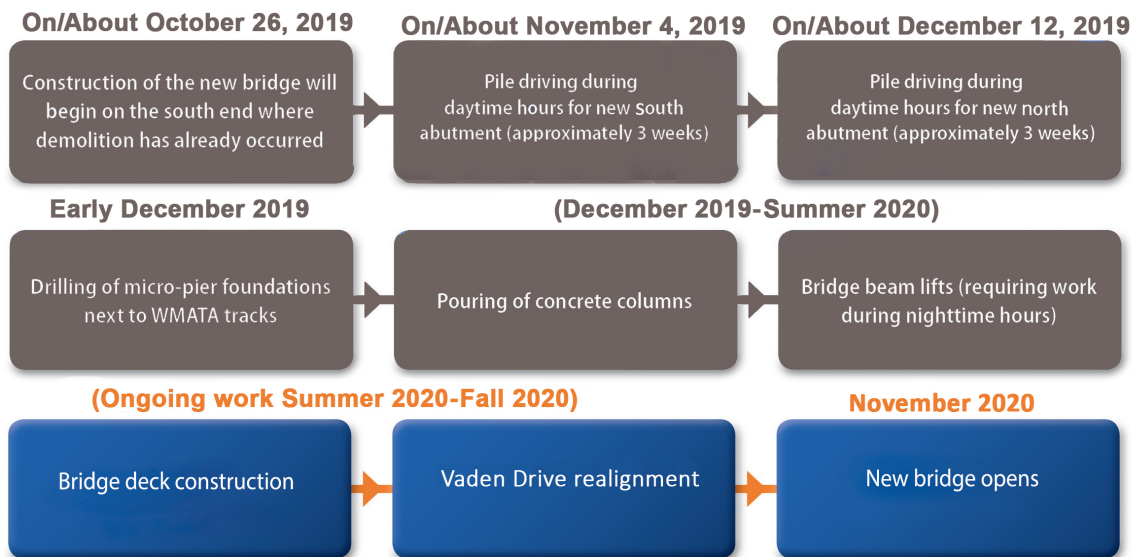

Pedestrian path under the north side of Vaden Drive will remain closed while construction continues on the retaining walls underneath and adjacent to the bridge.

Impact Control Measures

Not all construction activities will generate significant impacts, but when those intermittent activities do occur, all measures will be taken to minimize impacts as much as feasible.

During Construction:

- Lighting will be directed towards roadway
- Concrete pump and deliveries for final deck pour will be located on I-66
- Dust control measures will be in place
- Noise and vibration monitors will continue to be in use for all construction activities
- When possible, work will be conducted during daytime hours

For project updates and information on detours during the Vaden Drive closure visit:

outside.transform66.org/vienna

Questions about construction activities?

Construction Hotline: (703) 662-3892

E-mail: Outreach@fam66.us
